


Restoration Strategies Regional Water Quality Plan - Program Update

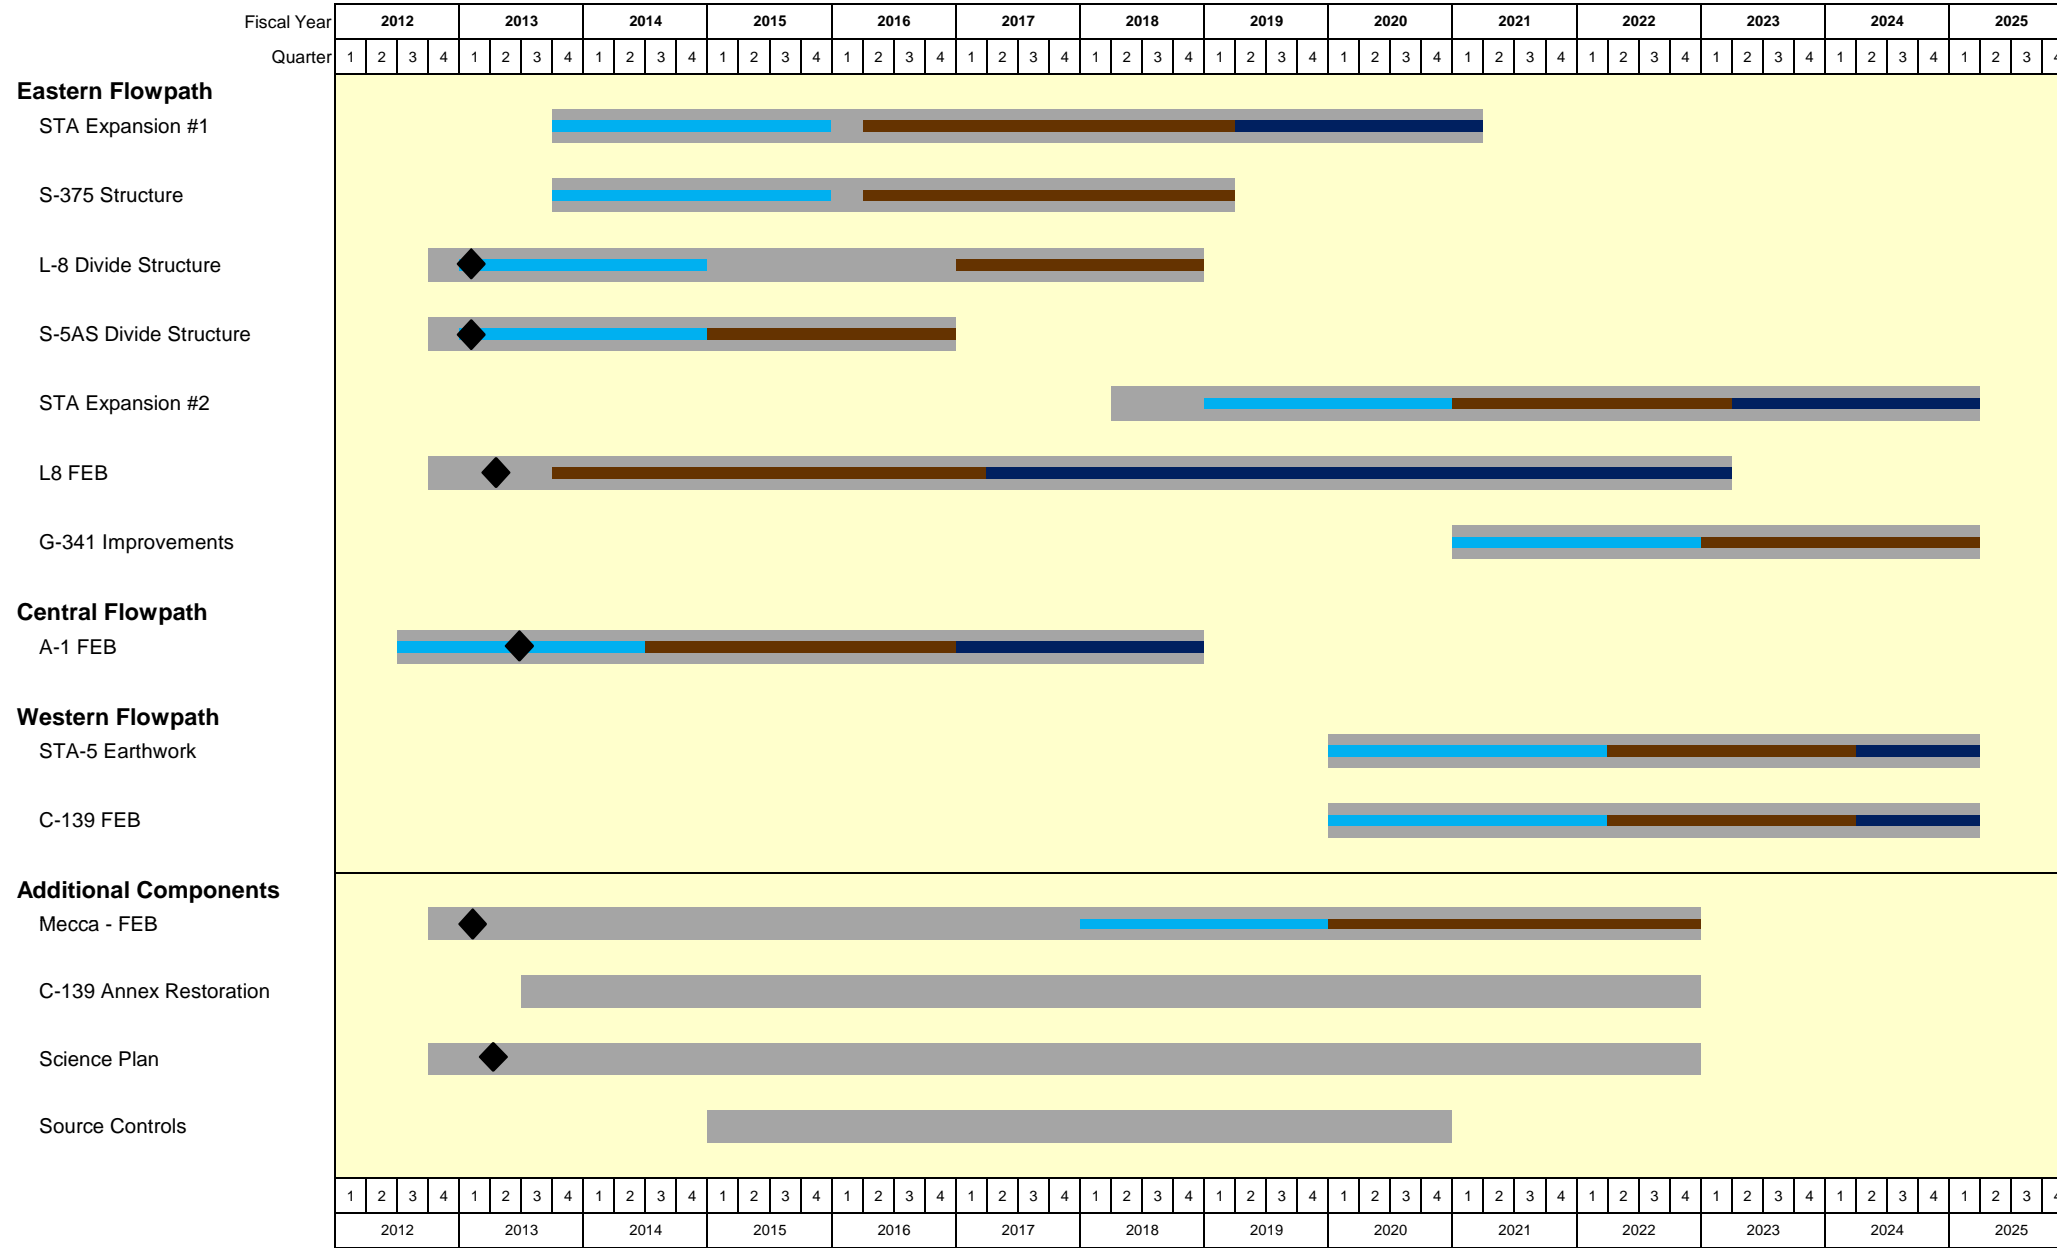

Project Status Highlights

Eastern Flowpath

- L-8 FEB**
 - Notice To Proceed issued on October 15th
 - Contractor is mobilizing temporary pumps to assist with emptying the reservoir
- L-8 Divide Structure and S-5AS Structure Modifications**
 - Currently in the preliminary design phase
 - Conducting a survey of the L-8 Canal to gather information to continue support of the development of a hydraulic model for conveyance
- Land Acquisition Activities**
 - land acquisition negotiations for Eastern Flowpath STA expansion continue:
 - Adjacent agricultural land owners to STA-1W
 - Department of the Interior (Strazulla wetlands and Snail farm land swap)
 - Negotiations are proceeding with Palm Beach County for a Loxahatchee River Project replacement storage feature (Mecca)

Central Flowpath

- A-1 FEB**
 - Work order is being executed for intermediate through final design
 - Interagency site visit in support of EIS took place on October 29th with the Corps, USEPA, USFWS and FDEP

Western Flowpath

- C-139 Annex Restoration**
 - Next Lake Belt Mitigation Committee meeting is currently scheduled for December 6th for consideration for approval.

Additional Components

- Science Plan**
 - Science Plan outline has been drafted
- Technical representatives**
 - First meeting occurred on November 6th

- Compliance Design phase
- Compliance Construction phase
- Project Duration
- Flooding and Optimization Period
- Project progress

Eastern Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
L8 Divide Structure - Initiate design	10/1/2012	9/10/2012	-21	
S-5AS Divide Structure - Initiate	10/1/2012	9/10/2012	-21	
* - is days ahead of schedule; + is days behind schedule				
FY13 Upcoming Milestones				
9/30/2013	STA-1W exp #1	complete land acquisition		
9/30/2013	STA-1W exp #1	Initiate Design		
9/30/2013	S-375 Structure modification	Initiate Design		

Central Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
A-1 FEB - Initiate design	4/1/2012	12/16/2010	-820	
A-1 FEB - submit permit applications	12/1/2012	9/17/2012	-74	
* - is days ahead of schedule; + is days behind schedule				
FY13 Upcoming Milestones				
3/1/2013	A-1 FEB	Design status report		
8/1/2013	A-1 FEB	Complete design		

Western Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
Upcoming Milestones				

STA = Stormwater Treatment Area
