


Restoration Strategies Regional Water Quality Plan - Program Update

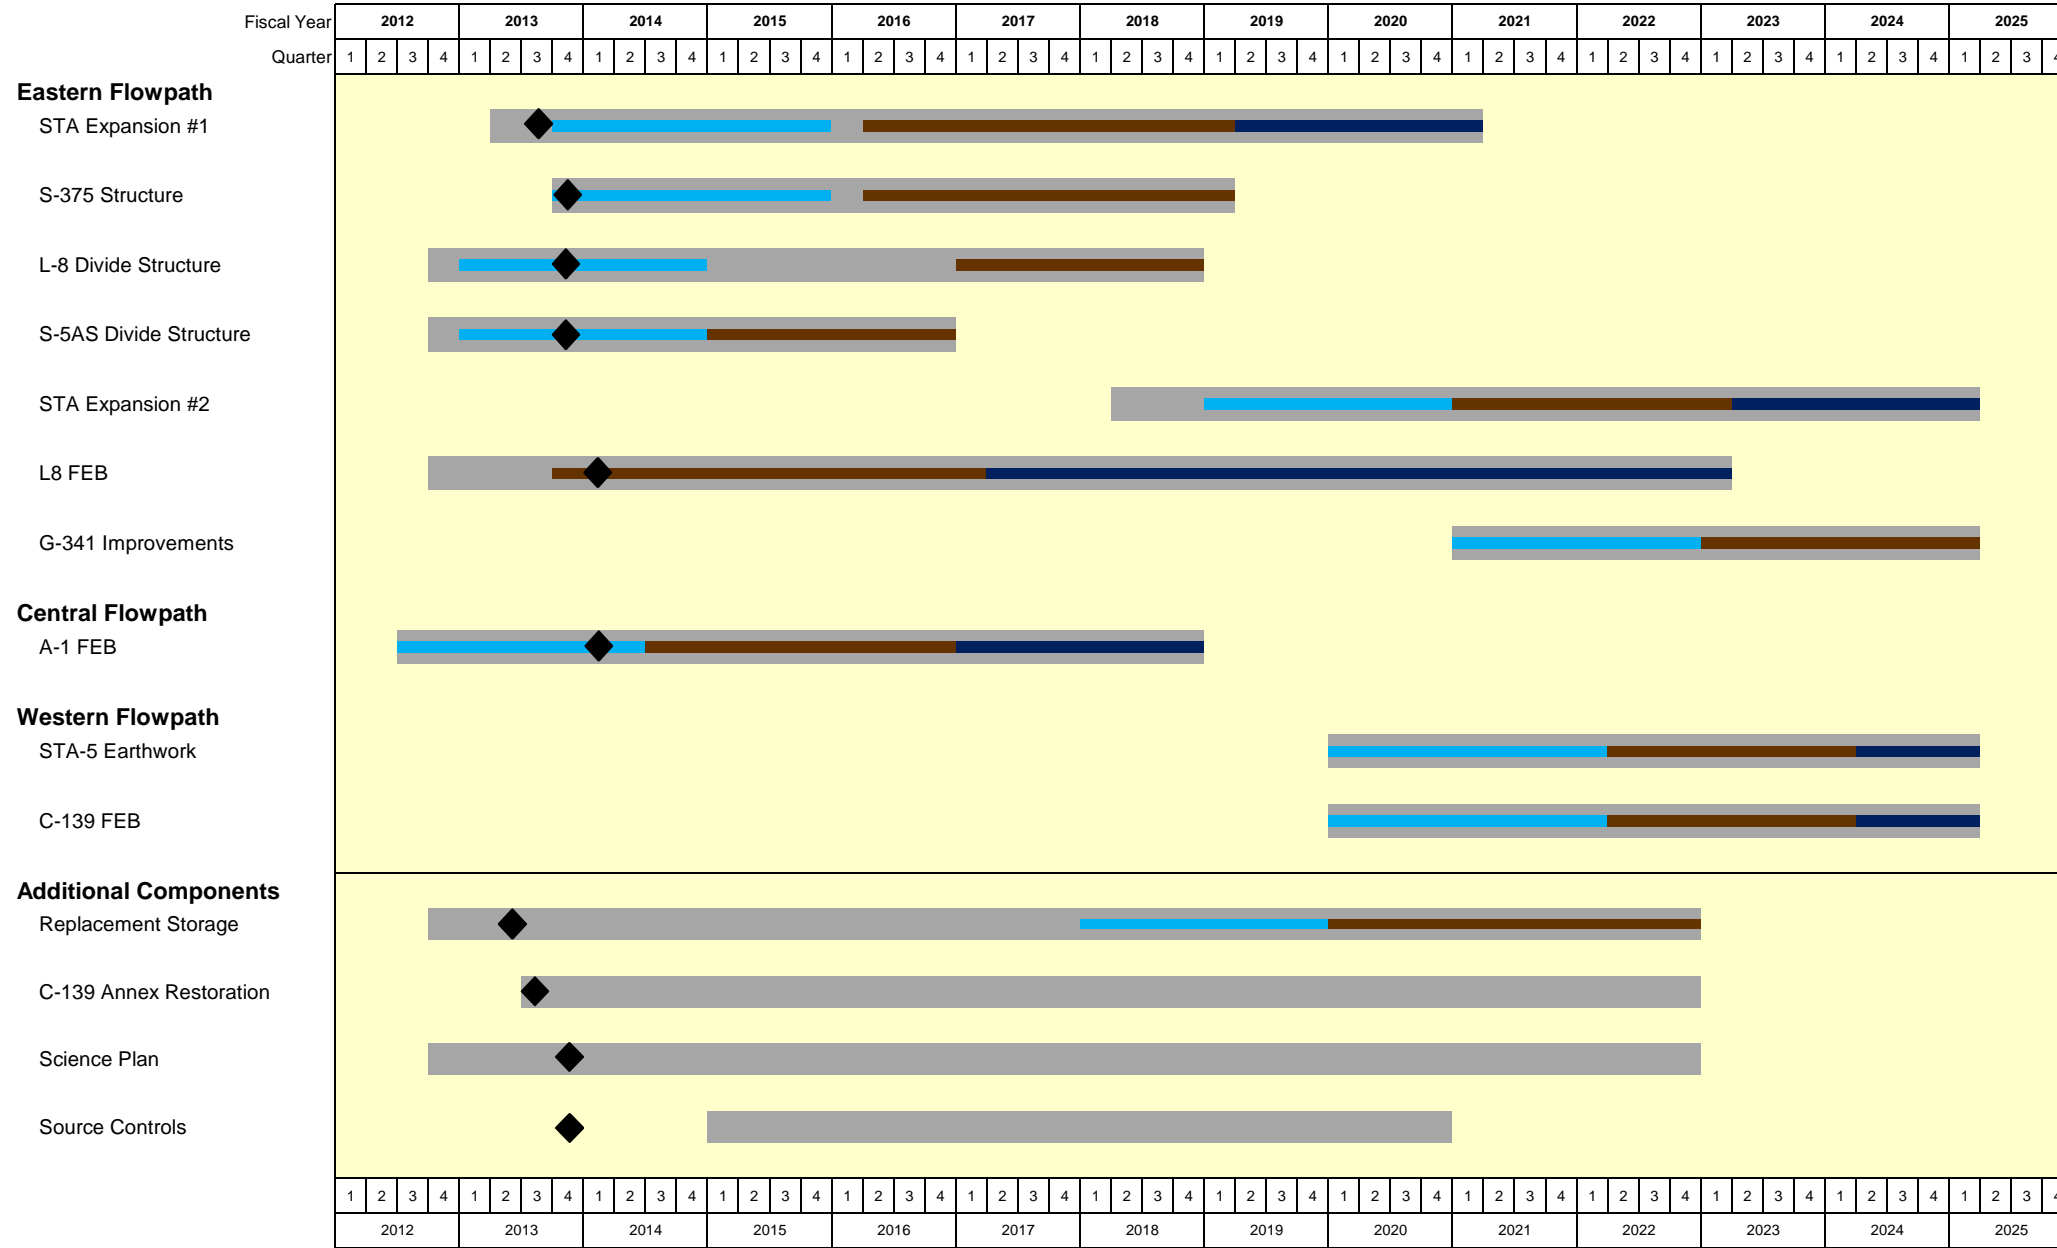

Project Status Highlights

Eastern Flowpath	
L-8 FEB	<ul style="list-style-type: none"> - Final pump station design submitted for District review - Dewatering is ongoing - USACE 408 Review process is underway
STA-1W Expansion	<ul style="list-style-type: none"> - Land acquisition negotiations underway
L-8 Divide Structure (G-541)	<ul style="list-style-type: none"> - Design is ongoing - Seepage analysis is underway
S-5AS Structure Modifications	<ul style="list-style-type: none"> - Continue with detailed design
S-375 Structure Expansion (G-716)	<ul style="list-style-type: none"> - Structure design is underway
-Land Acquisition Activities	<ul style="list-style-type: none"> - Acquisition negotiations for replacement storage ongoing

Central Flowpath

A-1 FEB	<ul style="list-style-type: none"> - EIS published in the Federal Register July 5 - Received Notice of Intent to Issue EFA construction and operations EFA permit from DEP
----------------	--

Western Flowpath

C-139 Annex Restoration	<ul style="list-style-type: none"> -Pre-restoration site assessments ongoing - Conceptual restoration phases being developed
--------------------------------	--

Additional Components

Science Plan	<ul style="list-style-type: none"> - Final Science Plan is available on the Restoration Strategies webpage: www.sfwmd.gov/restorationstrategies
Sub-Regional Source Controls	<ul style="list-style-type: none"> - Initiated 3-year cooperative agreement with EBWCD for canal cleaning demonstration project

- Compliance Design phase
- Compliance Construction phase
- Project Duration
- Flooding and Optimization Period
- Project progress

Eastern Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
L8 Divide Structure - Initiate design	10/1/2012	9/10/2012	-21	
Structure - Initiate design	10/1/2012	9/10/2012	-21	
L8 FEB - submit permit applications	1/31/2014	5/13/2013	-263	
* - is days ahead of schedule; + is days behind schedule				
FY13 Upcoming Milestones				
9/30/2013	STA-1W exp #1	complete land acquisition		
9/30/2013	STA-1W exp #1	Initiate Design		
9/30/2013	S-375 Structure modification	Initiate Design		

Central Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
A-1 FEB - Initiate design	4/1/2012	12/16/2010	-820	
A-1 FEB - submit permit applications	12/1/2012	9/17/2012	-74	
A-1 FEB - submit design status report	3/1/2013	2/1/2013	-30	
* - is days ahead of schedule; + is days behind schedule				
FY13 Upcoming Milestones				
8/1/2013	A-1 FEB	Complete design		

Western Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
Upcoming Milestones				

STA = Stormwater Treatment Area
