


Restoration Strategies Regional Water Quality Plan - Program Update

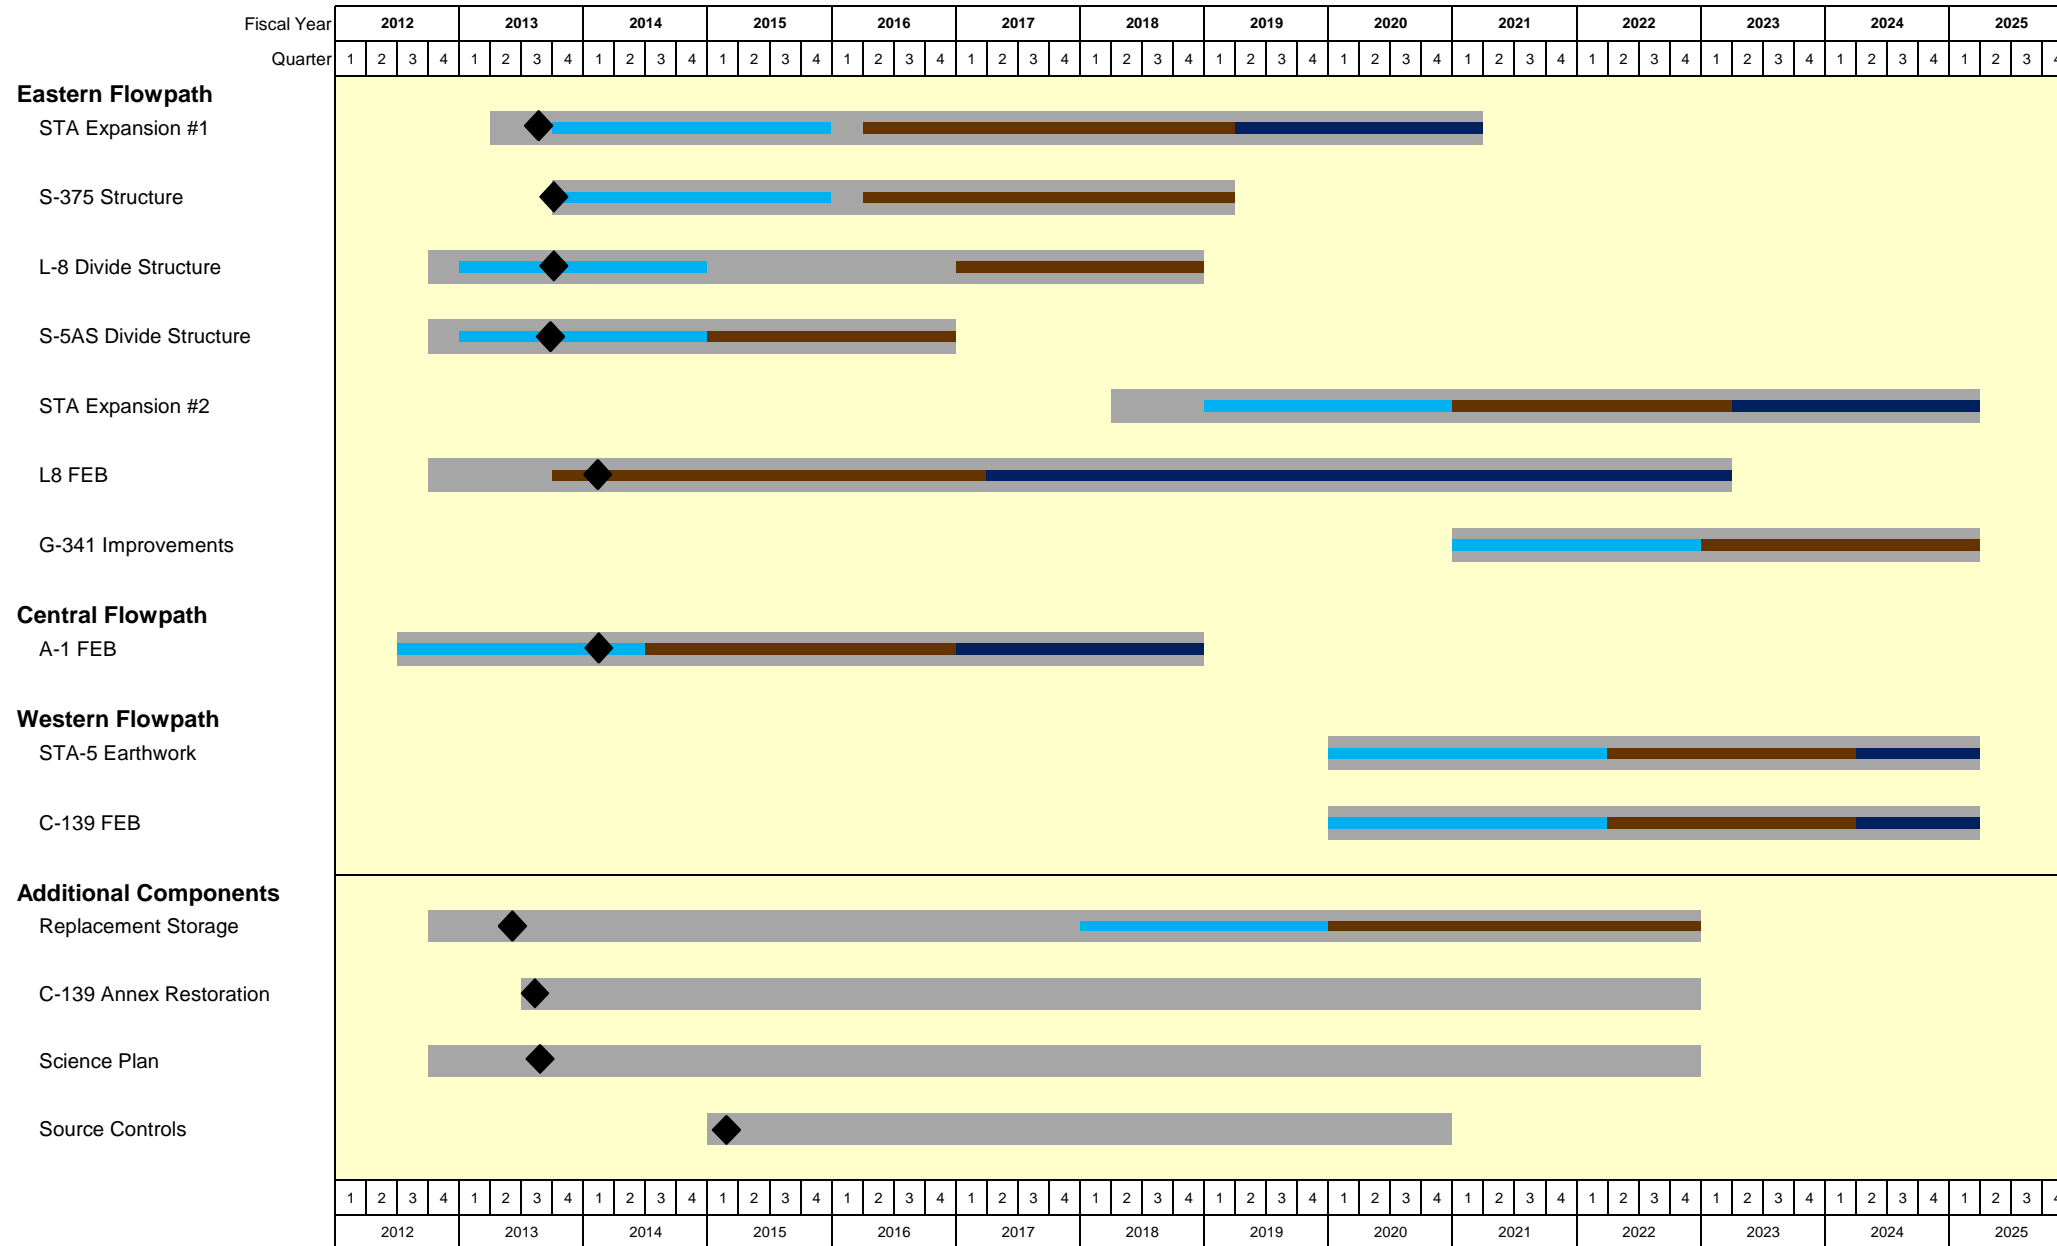

Project Status Highlights

Eastern Flowpath

- L-8 FEB**
- Final pump station design submitted for District review
  - Dewatering is ongoing
  - USACE 408 Review process is underway

- STA-1W Expansion**
- Project on hold pending land acquisition negotiations

- L-8 Divide Structure (G-541)**
- Design is ongoing
  - Seepage analysis is underway

- S-5AS Structure Modifications**
- Continue with detail design

- S-375 Structure Expansion (G-716)**
- Structure design is underway

- Land Acquisition Activities**
- Acquisition negotiations for replacement storage ongoing

Central Flowpath

- A-1 FEB**
- Final design submitted to District is under review
  - Received Notice of Complete Application from DEP for EFA permit

Western Flowpath

- C-139 Annex Restoration**
- Pre-restoration site assessments ongoing
  - Conceptual restoration phases being developed

Additional Components

- Science Plan**
- Final Science Plan published on June 10th
  - Hard copies delivered to DEP & EPA
  - Available on the Restoration Strategies webpage [www.sfwmd.gov/restorationstrategies](http://www.sfwmd.gov/restorationstrategies)

- Compliance Design phase
- Compliance Construction phase
- Project Duration
- Flooding and Optimization Period
- Project progress

| Eastern Flowpath - Recent Milestones  |           |           |           |          |
|---------------------------------------|-----------|-----------|-----------|----------|
| Project                               | Deadline  | Date Met  | *Days +/- | Status   |
| L8 Divide Structure - Initiate design | 10/1/2012 | 9/10/2012 | -21       | On Track |
| Structure - Initiate design           | 10/1/2012 | 9/10/2012 | -21       | On Track |
| L8 FEB - submit permit applications   | 1/31/2014 | 5/13/2013 | -263      | On Track |

\* - is days ahead of schedule; + is days behind schedule

| FY13 Upcoming Milestones |                              |                           |
|--------------------------|------------------------------|---------------------------|
| 9/30/2013                | STA-1W exp #1                | complete land acquisition |
| 9/30/2013                | STA-1W exp #1                | Initiate Design           |
| 9/30/2013                | S-375 Structure modification | Initiate Design           |

| Central Flowpath - Recent Milestones  |           |            |           |          |
|---------------------------------------|-----------|------------|-----------|----------|
| Project                               | Deadline  | Date Met   | *Days +/- | Status   |
| A-1 FEB - Initiate design             | 4/1/2012  | 12/16/2010 | -820      | On Track |
| A-1 FEB - submit permit applications  | 12/1/2012 | 9/17/2012  | -74       | On Track |
| A-1 FEB - submit design status report | 3/1/2013  | 2/1/2013   | -30       | On Track |

\* - is days ahead of schedule; + is days behind schedule

| FY13 Upcoming Milestones |         |                 |
|--------------------------|---------|-----------------|
| 8/1/2013                 | A-1 FEB | Complete design |

| Western Flowpath - Recent Milestones |          |          |           |        |
|--------------------------------------|----------|----------|-----------|--------|
| Project                              | Deadline | Date Met | *Days +/- | Status |
|                                      |          |          |           |        |
|                                      |          |          |           |        |

| Upcoming Milestones |  |  |
|---------------------|--|--|
|                     |  |  |
|                     |  |  |

STA = Stormwater Treatment Area
