


Restoration Strategies Regional Water Quality Plan - Program Update

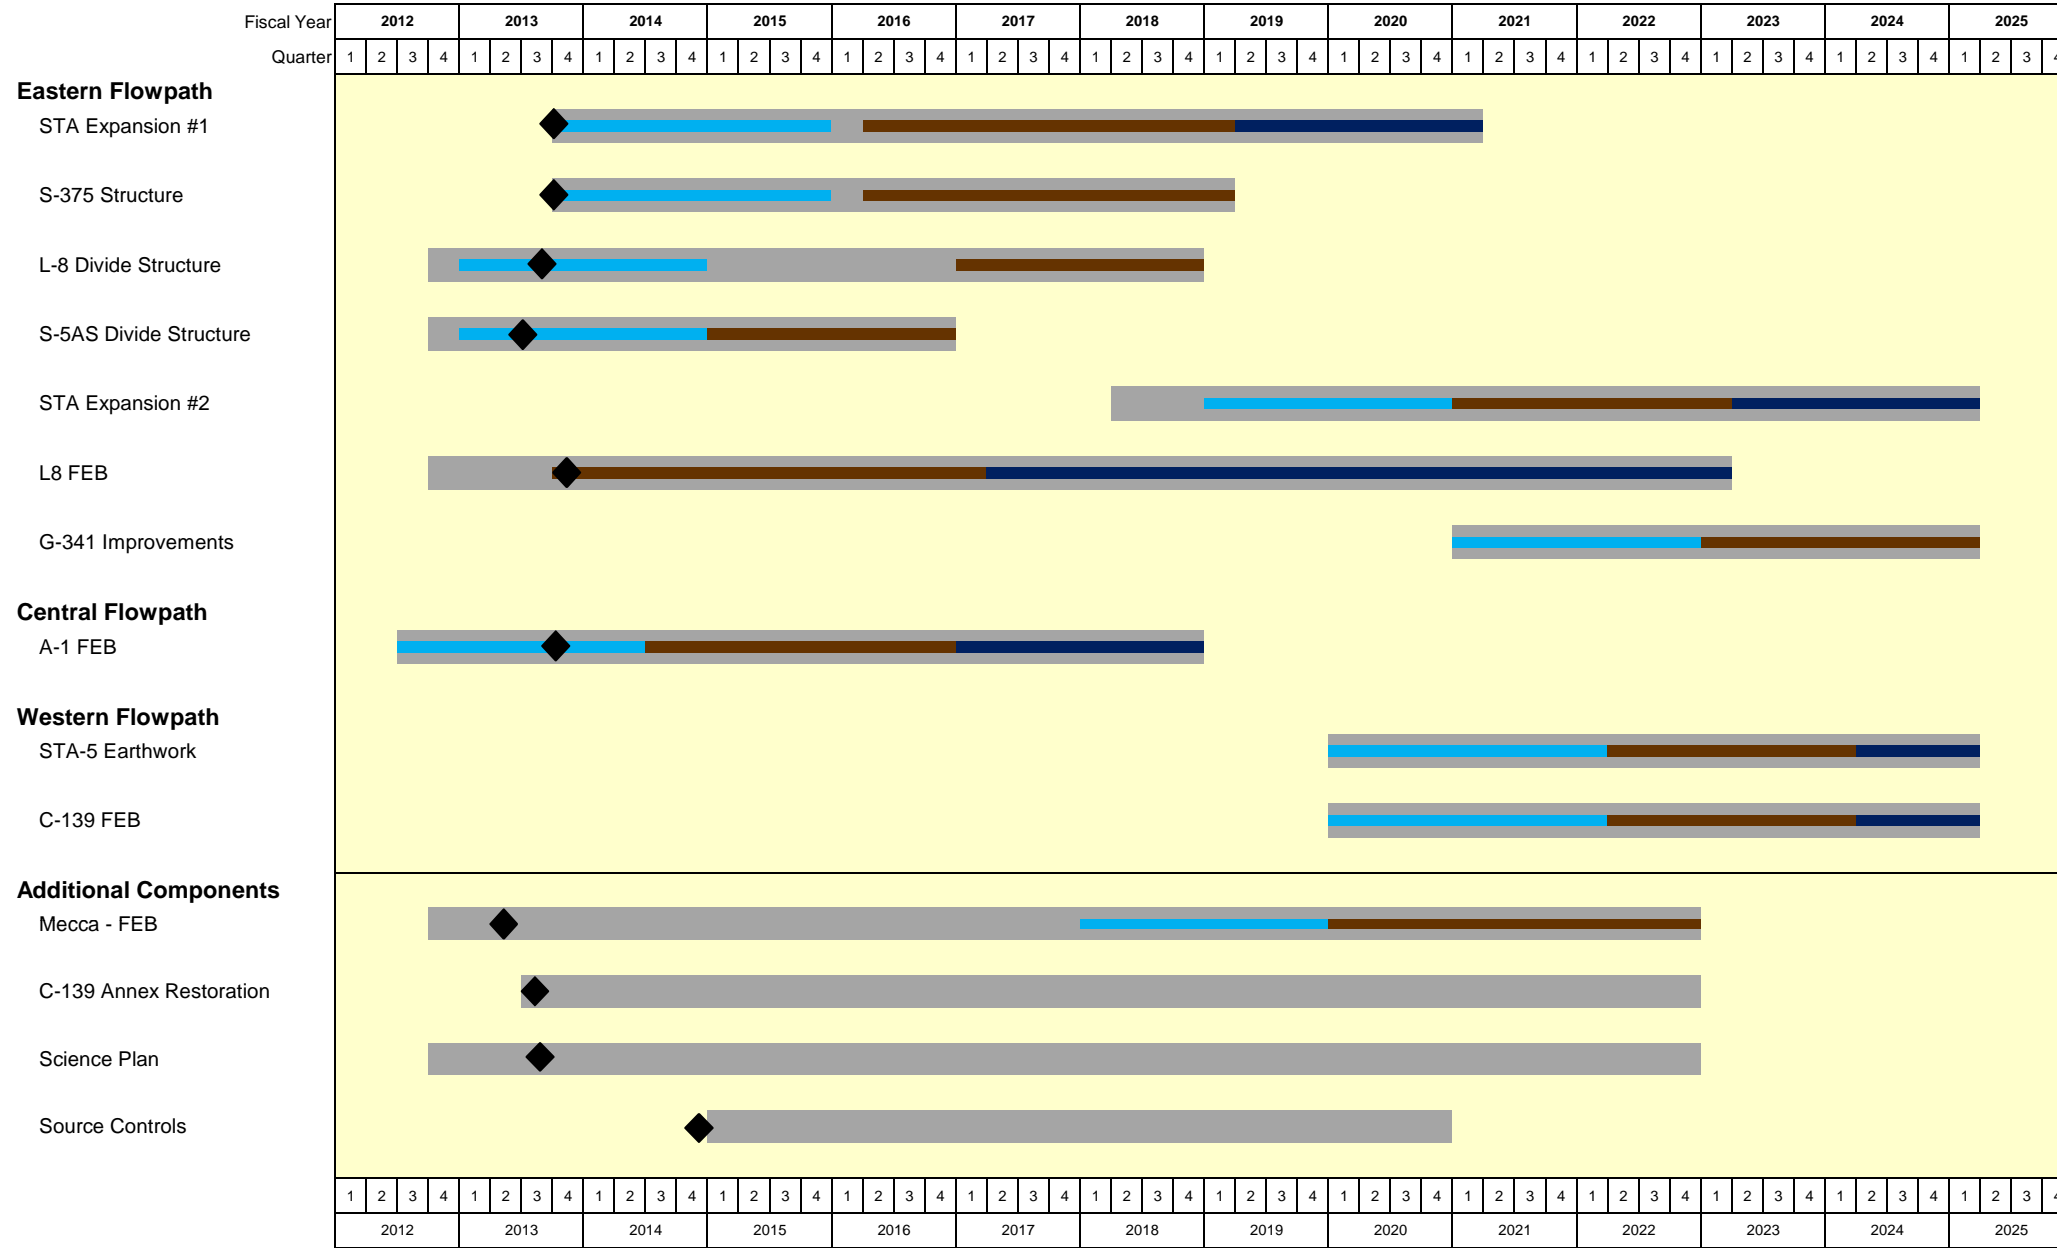

Project Status Highlights

Eastern Flowpath

- L-8 FEB**
 - 30% design review for the pump station, inflow and modifications has been reviewed
 - Federal and State permit application packages for the pump station is being prepared for submittal
- L-8 Divide Structure (G-541)**
 - Geotechnical data collection is underway
 - Permit pre-application meeting scheduled for the end of March with Federal and State regulatory agencies
 - Real Estate Certification complete for SFWMD Right of Way interest for construction
- S-5AS Structure Modifications**
 - Conceptual design is ongoing
 - Computational Fluid Dynamics Model is being calibrated
- S-375 Structure Expansion (G-716)**
 - Pre-design geotech and land surveys are being developed
- Land Acquisition Activities**
 - Acquisition negotiations for the Eastern Flowpath STA expansion continue
 - Negotiations are ongoing with Palm Beach County for a Loxahatchee River Restoration Project in-basin storage replacement feature (Mecca)

Central Flowpath

- A-1 FEB**
 - 60% design review is in process
 - Draft EIS was published and is undergoing public review

Western Flowpath

- C-139 Annex Restoration**
 - Pre-restoration site assessments are ongoing
 - Conceptual restoration phases being developed

Additional Components

- Science Plan**
 - Draft 5 year science plan and research studies developed and under internal review
- Technical representatives**
 - Next meeting is March 20th at District HQ to review draft research studies

- Compliance Design phase
- Compliance Construction phase
- Project Duration
- Flooding and Optimization Period
- Project progress

Eastern Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
L8 Divide Structure - Initiate design	10/1/2012	9/10/2012	-21	
S-5AS Divide Structure - Initiate	10/1/2012	9/10/2012	-21	
* - is days ahead of schedule; + is days behind schedule				
FY13 Upcoming Milestones				
9/30/2013	STA-1W exp #1	complete land acquisition		
9/30/2013	STA-1W exp #1	Initiate Design		
9/30/2013	S-375 Structure modification	Initiate Design		

Central Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
A-1 FEB - Initiate design	4/1/2012	12/16/2010	-820	
A-1 FEB - submit permit applications	12/1/2012	9/17/2012	-74	
A-1 FEB - submit design status report	3/1/2013	2/1/2013	-30	
* - is days ahead of schedule; + is days behind schedule				
FY13 Upcoming Milestones				
8/1/2013	A-1 FEB	Complete design		

Western Flowpath - Recent Milestones				
Project	Deadline	Date Met	*Days +/-	Status
Upcoming Milestones				

STA = Stormwater Treatment Area
