

## Restoration Strategies Program Update Governing Board – April 2014

### Eastern Flow Path

#### L-8 FEB

- Dewatering and construction of inflow works and outflow pump station ongoing

#### L-8 Divide Structure

- Submitted Milestone report to DEP – Complete Design
  - Concurrent Federal 408 review ongoing

#### STA-1W Expansion #1

- Land exchange – lease amendments require GB approval
  - Final environmental assessments are underway
    - Conceptual design is ongoing

#### S-375 Structure Expansion (G-716)

- Design is ongoing

#### S-5AS Divide Structure

- Final design is complete and under internal review

### Central Flow Path

#### A-1 FEB

- Construction is ongoing

### Western Flow Path

Projects to begin in 2019

### Additional Components

#### Science Plan

- Technical and University Services contract award to April GB approval

#### Sub-Regional Source Control


- Early start on two projects
- Conceptual project planning for FY15 is underway

#### Mecca - Replacement Feature

- Additional survey work initiated
- Subsequent land exchange negotiations ongoing for 150 acre gun range site within the Mecca parcel

Restoration Strategies Regional Water Quality Plan - Program Update

April - June 2014

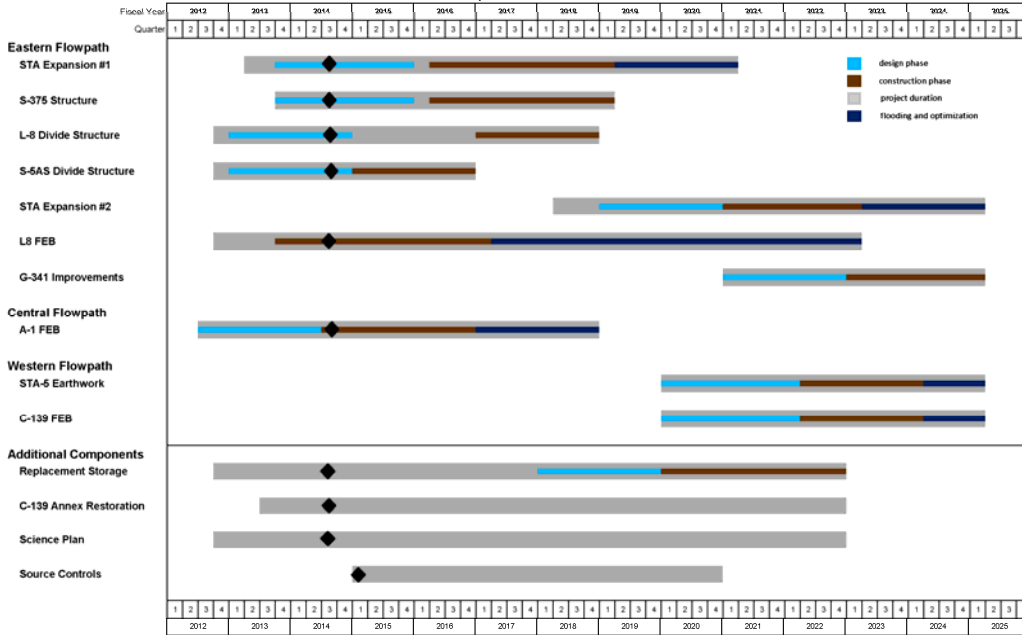

Restoration Strategies QB Timeline FY14 Q3.xlsx RS Timeline

3/20/2014 1:00 PM

Eastern Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
STA-1W exp #1: Land Acquisition	9/30/2013	4/1/2014		
L-8 FEB: Construction status report	3/1/2014	2/25/2014	+23	
STA-1W exp #1: Submit permit applications	7/30/2014			
L-8 Divide: Complete design	9/30/2014	3/5/2014	+209	
S-5AS Divide: Complete design	9/30/2014			

Central Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
A-1 FEB: Initiate construction	6/30/2014	10/10/2013	+263	

Western Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
Projects to begin in 2019				

\* + = days ahead; - = days behind
