

## Restoration Strategies Program Update Governing Board – August 2014

### Eastern Flow Path

#### L-8 FEB

- Dewatering and construction of inflow works and outflow pump station ongoing

#### L-8 Divide Structure

- Design complete

#### STA-1W Expansion #1

- Met Consent Order milestone in July for submit state and federal permit applications

#### S-375 Structure Expansion (G-716)

- Detailed design has transitioned to an external design contract

#### S-5AS Divide Structure

- Design complete

### Central Flow Path

#### A-1 FEB

- Construction is ongoing

### Western Flow Path

Projects to begin in 2019

### Additional Components

#### Science Plan

- Initial eight projects in implementation
- Contracts to initiate fieldwork are being prepared


#### Sub-Regional Source Control

- Conceptual project planning for FY15 is underway

#### Mecca - Replacement Feature

- Conceptual planning and site analysis is being developed to determine start of design

Restoration Strategies Regional Water Quality Plan - Program Update  
July - September 2014

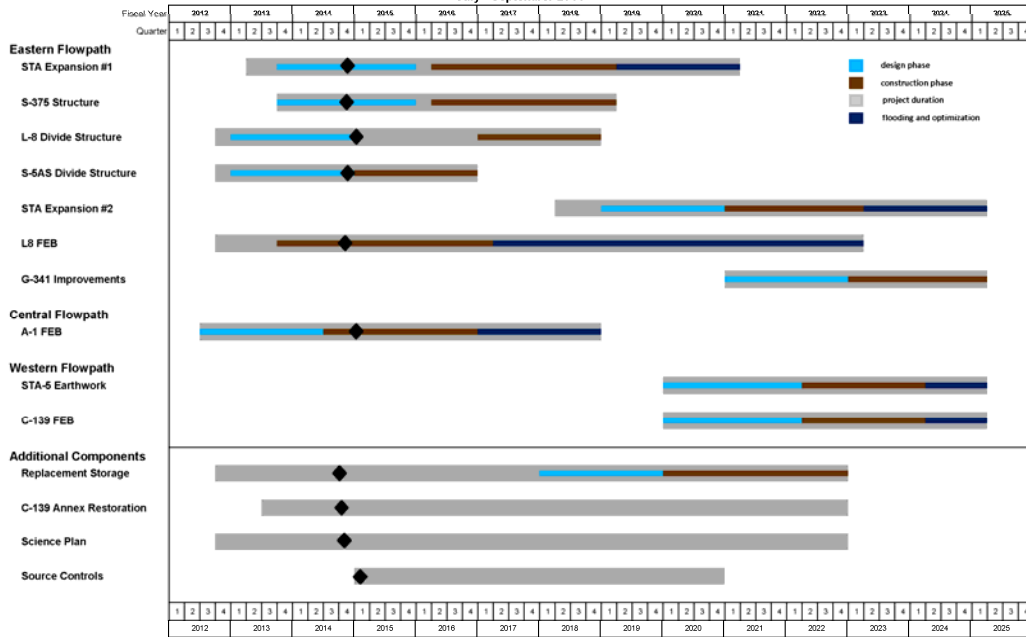

Restoration Strategies QB timeline FY14 Q4.xlsx RS Timeline

6/30/2014 9:59 AM

Eastern Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
STA-1W exp #1: Complete Land Acquisition	9/30/2013	4/28/2014	-46	
L-8 FEB: Construction status report	3/1/2014	2/25/2014	+23	
STA-1W exp #1: Submit permit applications	7/30/2014	7/23/2014	+7	
L-8 Divide: Complete design	9/30/2014	3/5/2014	+209	
S-5AS Divide: Complete design	9/30/2014	4/17/2014	+166	

Central Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
A-1 FEB: Initiate construction	6/30/2014	10/10/2013	+263	

Western Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
Projects to begin in 2019				

\* + = days ahead; - = days behind
