

Restoration Strategies Program Update Governing Board – July 2014

Eastern Flow Path

L-8 FEB

- Dewatering and construction of inflow works and outflow pump station ongoing

L-8 Divide Structure

- Received FDEP construction permit
- USACE 404 30-day public notice sent on June 12th

STA-1W Expansion #1

- Preliminary design is underway
- Permit applications for construction and operations are being prepared for submittal

S-375 Structure Expansion (G-716)

- In detailed design phase

S-5AS Divide Structure

- Design is complete

Central Flow Path

A-1 FEB

- Construction is ongoing

Western Flow Path

Projects to begin in 2019

Additional Components

Science Plan

- Initial eight projects in implementation
- Contracts to initiate fieldwork are being prepared


Sub-Regional Source Control

- Conceptual project planning for FY15 is underway

Mecca - Replacement Feature

- Conceptual planning and site analysis is being developed to determine start of design

Restoration Strategies Regional Water Quality Plan - Program Update
July - September 2014

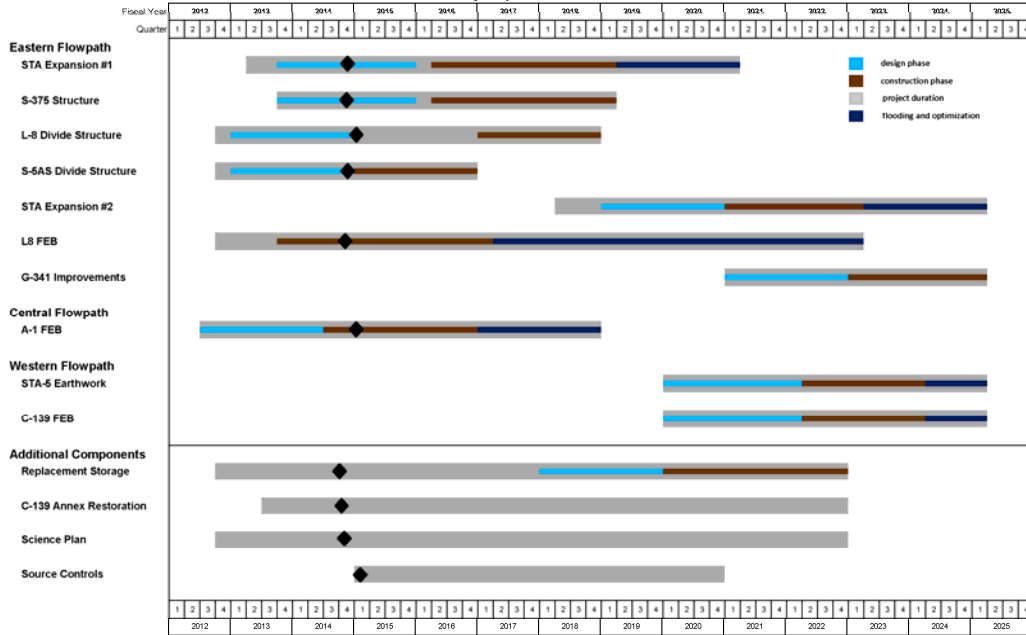

Restoration Strategies QB timeline FY14 Q4.xlsx RS Timeline

9/30/2014 9:59 AM

Eastern Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
STA-1W exp #1: Complete Land Acquisition	9/30/2013	4/28/2014	-46	
L-8 FEB: Construction status report	3/1/2014	2/25/2014	+23	
STA-1W exp #1: Submit permit applications	7/30/2014			
L-8 Divide: Complete design	9/30/2014	3/5/2014	+209	
S-5AS Divide: Complete design	9/30/2014	4/17/2014	+166	

Central Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
A-1 FEB: Initiate construction	6/30/2014	10/10/2013	+263	

Western Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
Projects to begin in 2019				

* + = days ahead; - = days behind
