

Restoration Strategies Program Update Governing Board – March 2014

Eastern Flow Path

L-8 FEB

- Met Construction Status Report Milestone on 2/7/2014
- Received Corps 404 permit for the pump station and inflow works in L-8 levee

L-8 Divide Structure

- Final design plans are under review
- Concurrent Federal 408 review ongoing

STA-1W Expansion #1

- Final environmental assessments are underway
 - Conceptual design is underway

S-375 Structure Expansion (G-716)

- 30% design complete

S-5AS Divide Structure

- Final design plans are under review

Central Flow Path

A-1 FEB

- Construction is ongoing

Western Flow Path

Projects to begin in 2019

Additional Components

Science Plan

- Technical and University Services contract – proposals under review


Sub-Regional Source Control

- Early start on two projects
- Conceptual project planning for FY15 is underway

Replacement Feature

- Mecca parcel is being leased while the project is in design
- Subsequent land exchange negotiations ongoing for 150 acre gun range site within the Mecca parcel

Restoration Strategies Regional Water Quality Plan - Program Update
January - March 2014

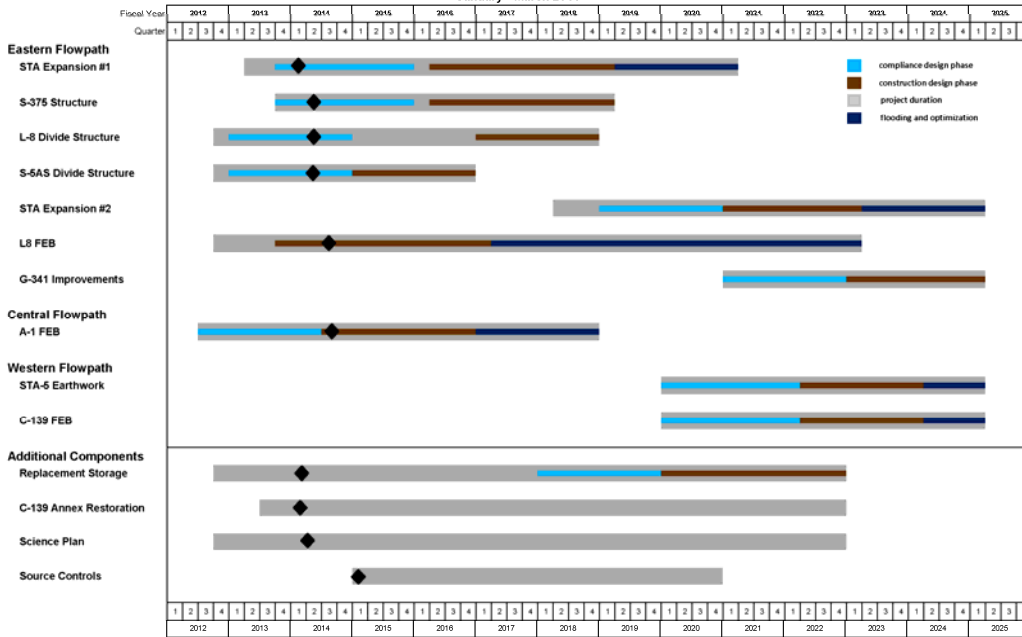

Restoration Strategies QB Timeline FY14 Q2.xlsx RS Timeline

2/4/2014 4:00 PM

Eastern Flow Path Milestones				
Project	Deadline	Date met	*Days +/-	Status
STA-1W exp #1: Land Acquisition	9/30/2013	In process		
L-8 FEB: Construction status report	3/1/2014	2/7/2014	+23	
STA-1W exp #1: Submit permit applications	7/30/2014			
L-8 Divide: Complete design	9/30/2014			
S-5AS Divide: Complete design	9/30/2014			

Central Flow Path Milestones				
Project	Deadline	Date met	*Days +/-	Status
A-1 FEB: Initiate construction	6/30/2014	10/10/2013	+263	

Western Flow Path Milestones				
Project	Deadline	Date met	*Days +/-	Status
Project to begin in 2019				

* + = days ahead; - = days behind
