

Restoration Strategies Program Update Governing Board – May 2014

Eastern Flow Path

L-8 FEB

- Dewatering and construction of inflow works and outflow pump station ongoing

L-8 Divide Structure

- Received notice of complete construction permit application from DEP
 - Concurrent Federal 408 review ongoing

STA-1W Expansion #1

- Land exchange final on April 23 – submitted Milestone report to DEP – complete Land Acquisition
 - Final environmental assessments are ongoing
 - Preliminary design has started

S-375 Structure Expansion (G-716)

- Design is ongoing

S-5AS Divide Structure

- Submitted Milestone report to DEP – Complete Design

Central Flow Path

A-1 FEB

- Construction is ongoing

Western Flow Path

Projects to begin in 2019

Additional Components

Science Plan

- Initial eight projects in implementation, statements of work for recently approved technical services contracts being developed


Sub-Regional Source Control

- Early start on two projects
- Conceptual project planning for FY15 is underway

Mecca - Replacement Feature

- Additional survey work initiated

Restoration Strategies Regional Water Quality Plan - Program Update
April - June 2014

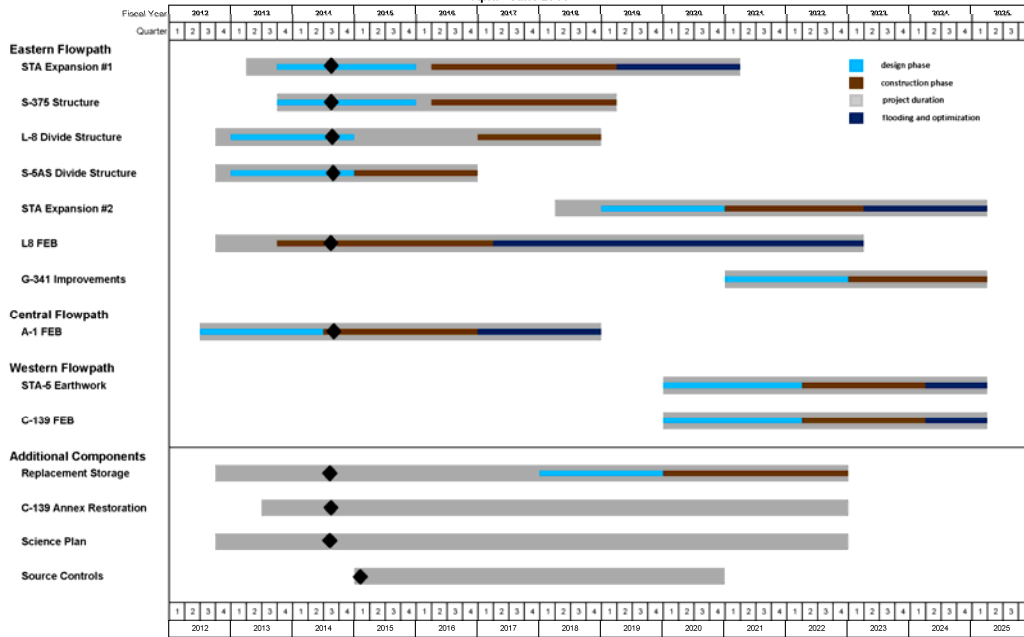

Restoration Strategies QB Timeline FY14 Q3.xlsx RS Timeline

3/20/2014 1:00 PM

Eastern Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
STA-1W exp #1: Complete Land Acquisition	9/30/2013	4/25/2014	-46	On Track
L-8 FEB: Construction status report	3/1/2014	2/25/2014	+23	On Track
STA-1W exp #1: Submit permit applications	7/30/2014			On Track
L-8 Divide: Complete design	9/30/2014	3/5/2014	+209	On Track
S-5AS Divide: Complete design	9/30/2014	4/17/2014	+166	On Track

Central Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
A-1 FEB: Initiate construction	6/30/2014	10/10/2013	+263	On Track

Western Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
Projects to begin in 2019				On Track

* + = days ahead; - = days behind
