

Restoration Strategies Program Update Governing Board – September 2015

Eastern Flow Path

L-8 FEB

Inflow spillway – complete and operational
Outflow pump station in construction, nearing completion
Contractor has started filling the FEB

L-8 Divide Structure

In construction

STA-1W Expansion #1

Final design complete, project out for bid

S-375 Structure Expansion (G-716)

Final design complete, project out for bid

S-5AS Divide Structure

In construction

G-341 Related Improvements

L-16 Bolles East Canal Phase 1 Segment 1 - In design

Central Flow Path

A-1 FEB

Construction substantially - complete
Final structure inspections – complete
Initial filling - commenced

Western Flow Path

Projects to begin in 2018

Additional Components

Science Plan

Eight STA related research projects on going to improve treatment performance


Sub-Regional Source Control

Project planning for FY15 is ongoing
Two new source control projects are underway

Mecca - Replacement Feature

In design

Restoration Strategies Regional Water Quality Plan - Program Update
July - September 2015

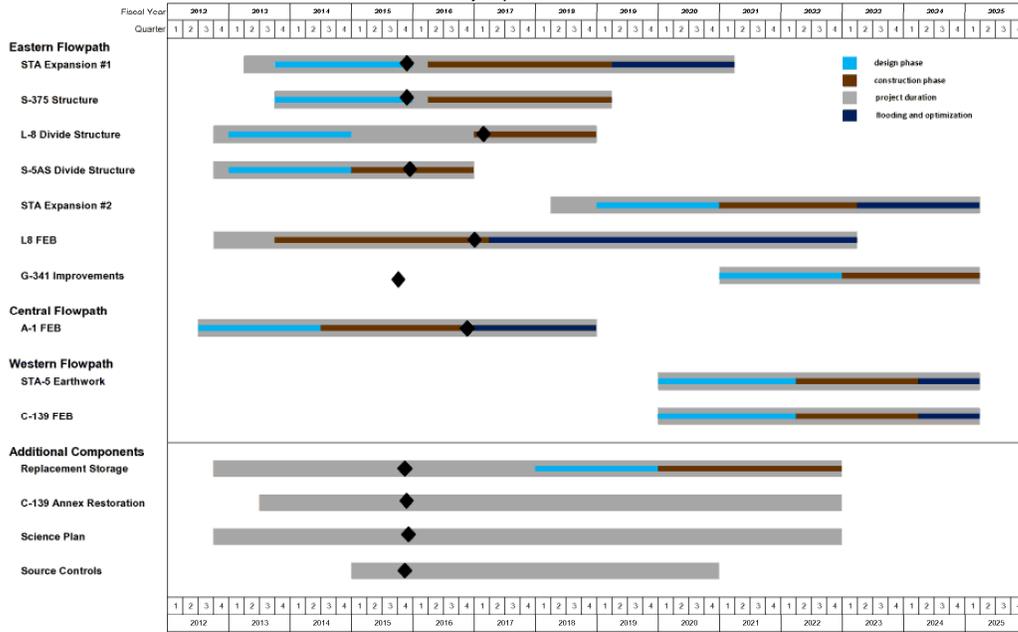

Restoration Strategies GIS Timeline FY15 Q4.xlsx RS Timeline

7/23/2015 9:08 AM

Eastern Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
S-5AS Divide: Initiate Construction	10/1/2014	9/15/2014	+15	On Track
L-8 Divide: Initiate Construction	10/1/2016	9/15/2014	+745	On Track
L-8 FEB: Construction Status Report	3/1/2015	2/26/2015	+2	On Track
S-375 Structure Expansion: Complete Design	7/30/2015	7/22/2015	+8	On Track
STA-1W Expansion #1: Complete Design of STA	7/30/2015	6/22/2015	+37	On Track

Central Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
A-1 FEB: Construction Status Report	3/1/2015	2/26/15	+2	On Track

Western Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
Projects to begin in 2019				

* + = days ahead; - = days behind
