

Restoration Strategies Program Update Governing Board – October 2015

Eastern Flow Path

L-8 FEB

Inflow spillway – complete and operational
Outflow pump station in construction, nearing completion
Contractor has started filling the FEB

L-8 Divide Structure

In construction

STA-1W Expansion #1

Final design complete, project out for bid
Florida Department for Environmental Protection Everglades Forever Act Permit issued for construction

S-375 Structure Expansion (G-716)

Final design complete, project out for bid

S-5AS Divide Structure

In construction

G-341 Related Improvements

L-16 Bolles East Canal Phase 1 Segment 1 - In construction

Central Flow Path

A-1 FEB

Construction complete
Initial filling – commenced
Operational Testing and Monitoring Period Starting

Western Flow Path

Projects to begin in 2018

Additional Components

Science Plan

Eight STA related research projects on going to improve treatment performance
Seven technical publications complete

Sub-Regional Source Control


FY15 – FY16 Project Feasibility study initiated
Two new source control projects are underway

Mecca - Replacement Feature

In design

For more information go to www.sfwmd.gov/restorationstrategies

Restoration Strategies Regional Water Quality Plan - Program Update
October - December 2016

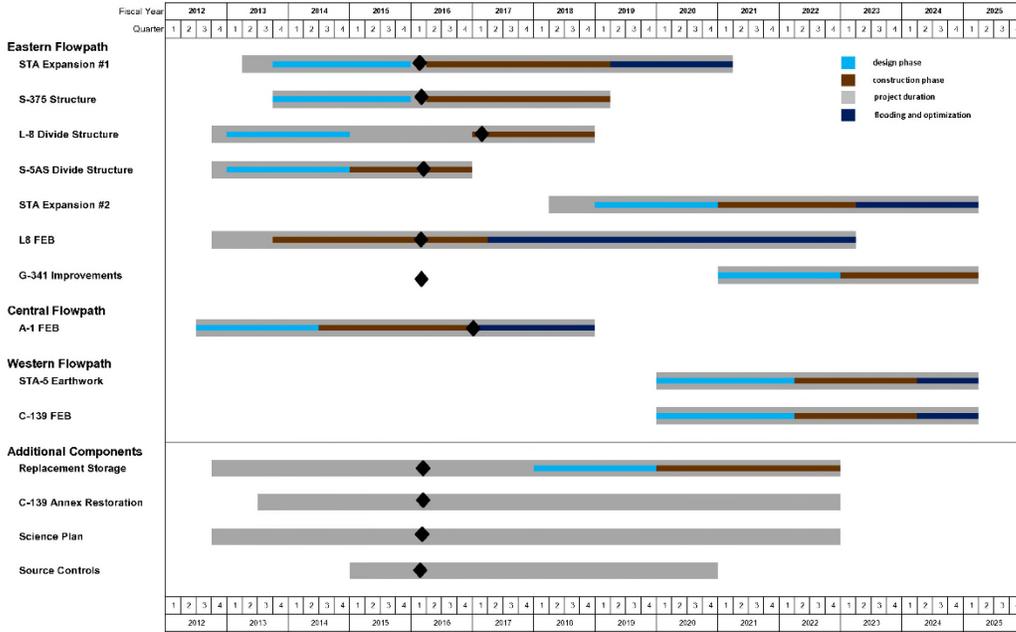

Restoration Strategies GR timeline FY16 Q1.xlsx RS Timeline

9/30/2015 8:24 AM

Eastern Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
STA-1W Expansion #1: Initiate Construction of STA	1/31/2016			
S-375 Structure Expansion: Initiate Construction	1/31/2016			
S-5AS Divide Structure: Complete Construction	9/30/2016			

Central Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
A-1 FEB: Construction Status Report	3/1/2016			
A-1 FEB: Completion of Construction	7/30/2016	9/28/2015	+337	

Western Flow Path Milestones				
Project	Deadline	Date submitted	*Days +/-	Status
Projects to begin in 2019				

* + = days ahead; - = days behind
