

WRAC Recreation Issue Workshop

November 14, 05

Status Updates Storm Water Treatment Areas CERP Projects

Jerry Krenz, AICP

South Florida Water Management District

STORMWATER TREATMENT AREAS

- **Public Access design SOW**
 - Design and construction FY 06
 - STA1W – North side
 - STA 3/4 – Griffin Pits
- **STA 3/4 SE corner**



STORMWATER TREATMENT AREAS

- **Duck Hunting**
 - Use variable traffic and parking
 - Will review every Wednesday for the weekend



STORMWATER TREATMENT AREAS

- **Duck Hunting**
 - **Hurricane impacts FPL issues**
 - **Will review with FPL no later than this Wednesday for the weekend**
 - **Cancelled Nov. 12 scouting day**
 - **Notification of cancellation comments**



CERP UPDATES

- **Master Recreation Plan, MRP, Update**
- **Acc8 and CERP projects**
 - **STAs and Impoundments**



MRP UPDATE



CERP Master Recreation Plan

- GIS task order delayed by Katrina and Wilma
- Other task orders to follow
- Final Draft July 07



STA PROJECT UPDATE

Long-Term Plan Revisions for STA Recreational Facilities

		Current LTP	Proposed LTP		
		Design	Build	Design	Build
■	STA-1E Ph 1	FY05	FY06	FY06	FY07
■	STA-1E Ph 2	FY06	FY07	FY06	FY07
■	may change location				
■	STA-1W	FY05	FY06	FY06	FY06
■	STA-3/4 Ph 1	FY05	FY06	FY06	FY06
■	STA-3/4 Ph 2	FY06	FY07	FY06	FY07

FY - Fiscal year October 1 to September 30




STA PROJECT UPDATE



- Long-Term Plan revisions for STA-1E Recreational Facilities

- Currently evaluating different sites

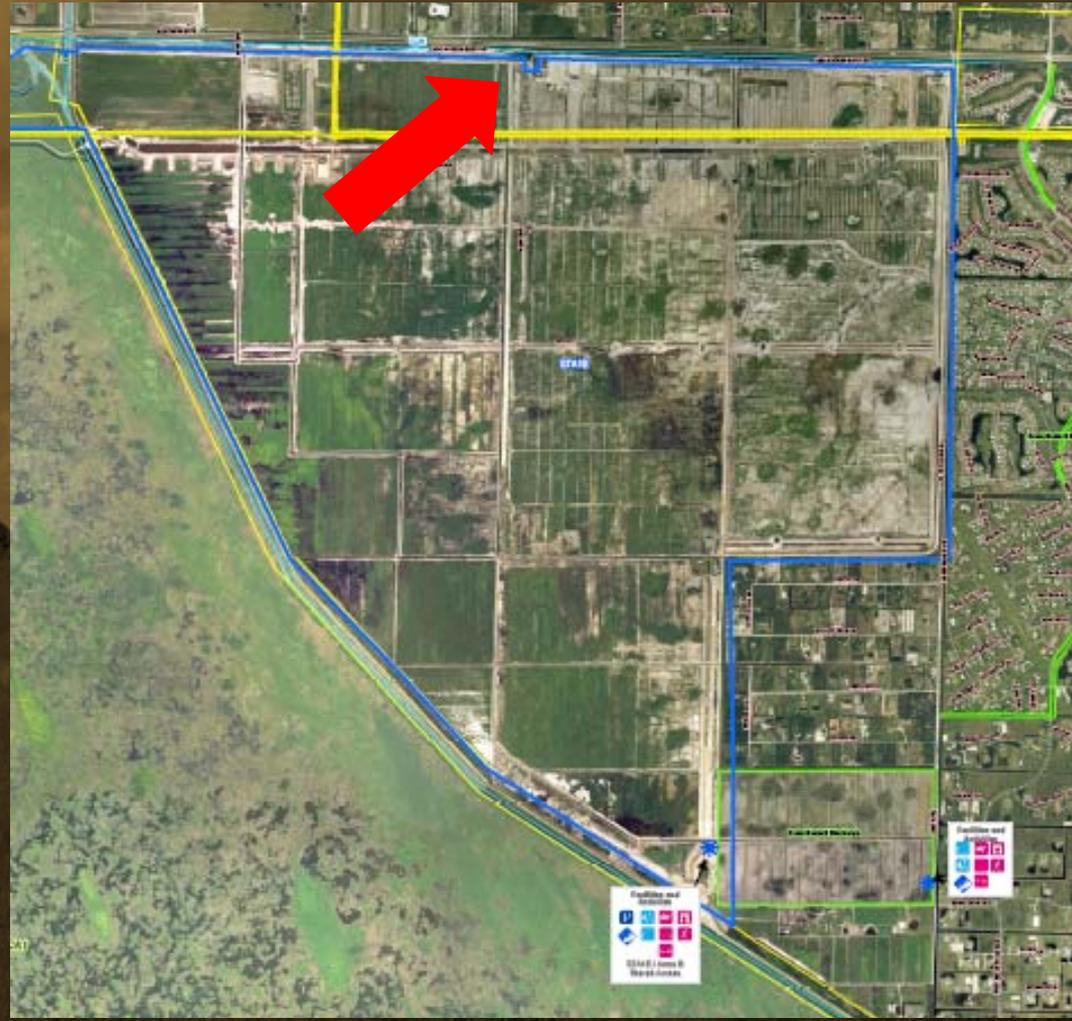


STA PROJECT UPDATE

- 
- **Long-Term Plan revisions for STA Recreational Facilities**
 - EAA Compartment B or STA-2,
 - EAA Compartment C or STA-5/6
 - STA 5 Recreational Facilities at Deer Fence Rd.
 - **Built as part of the Acceler8 construction**
 - **Dates tied to Acceler8 construction dates**
 - **Current Buildout construction dates are: ***
 - Flow capable treatment areas - December 2008
 - Complete all construction – varies by STA
 - Recreational Facilities - estimated completion 2009

* Nov. 2005 dates shown, construction dates are subject to change

STA PROJECT UPDATE

- Long Term Plan STA Recreational Facilities STA 2, 5, & 6

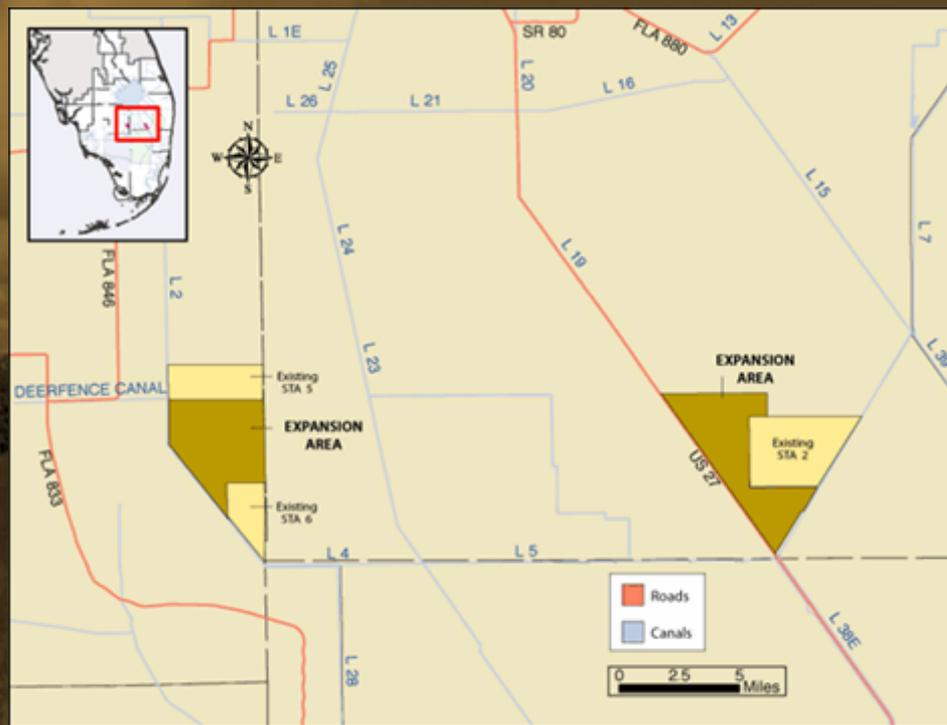

- COMPARTMENT C
 - HENDRY COUNTY
 - 8,800 ACRES

- COMPARTMENT B
 - PALM BEACH COUNTY
 - 9,500 ACRES

STA PROJECT UPDATE

- **Long-Term Plan revisions for STA Recreational Facilities**
 - **Public access for bird watching and duck hunting on STAs 1W, 3/4 and 5 will continue to be coordinated with construction to allow, as possible, activities that do not interfere with the purpose of the project**




CERP ACCELER8 PROJECT UPDATES

- Broward County WPA
 - Second Draft PIR
 - Potential SW Ranches site
 - BODR early 2006



CERP ACCELER8 PROJECT UPDATES

- C- 43 Reservoir Littoral Zones
 - In ASR ROW
 - Reviewing Littoral Zones Design

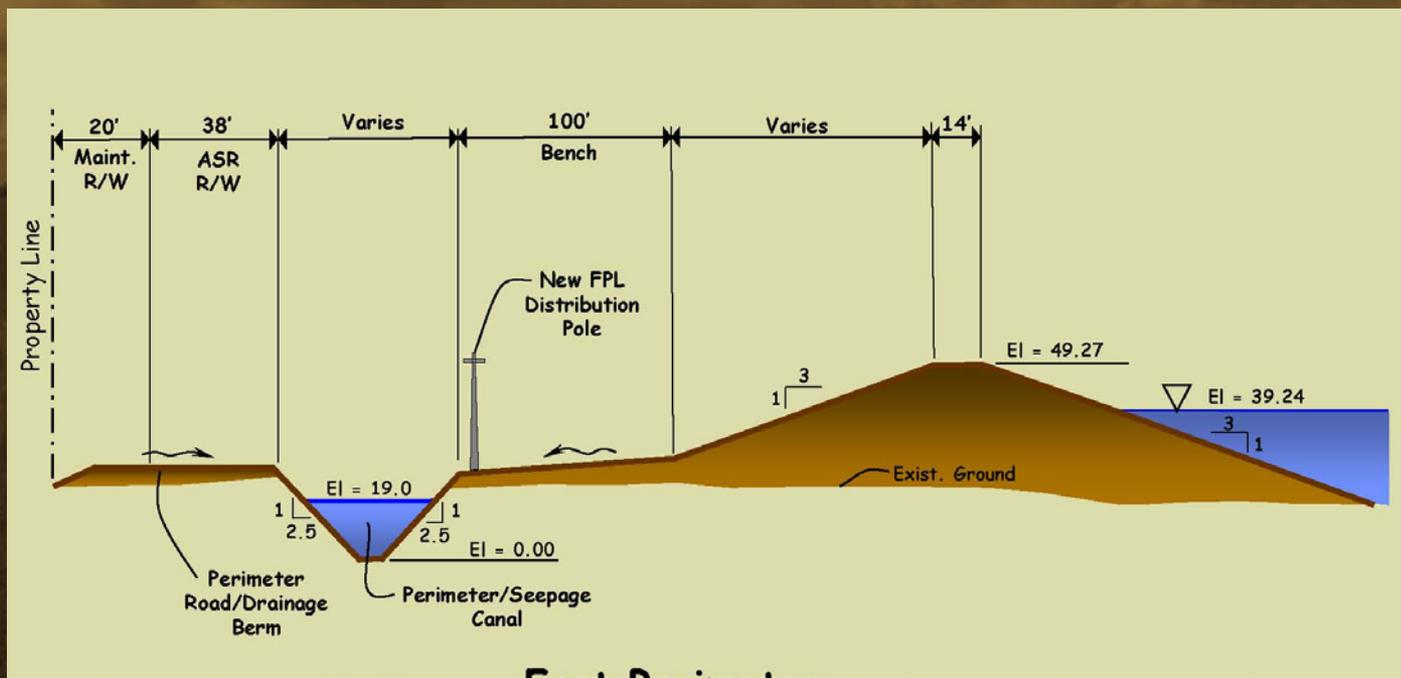

DISCUSSION



Jerry Krenz, AICP
Program Manager, Everglades Recreation

jkrenz@sfwmd.gov
(561) 682-6746
